

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	3 October 2026
Team ID	SWTID-2026-4089
Project Name	Auto Ticket Classification Using Floor Designer
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Proposed four-sprint backlog for automatic ticket classification and routing using Floor Designer.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint 1	Ticket Intake	US-01	As a support agent, I want new tickets normalized so each request starts with consistent fields.	3	High	Analyst / Dev
Sprint 1	Classification	US-02	As a support agent, I want tickets labeled with category and subcategory from configured rules.	5	High	Workflow Dev
Sprint 2	Priority	US-03	As a support lead, I want priority set from service and urgency signals so urgent work is surfaced.	3	High	Analyst / Dev
Sprint 2	Routing	US-04	As a support agent, I want tickets routed to the right group with a notification so ownership is clear.	5	High	Workflow Dev
Sprint 3	Human Review	US-05	As an agent, I want low-confidence tickets sent to triage with the reason visible so uncertain cases are checked.	3	High	Workflow Dev
Sprint 3	Feedback & Audit	US-06	As a reviewer, I want corrections logged so decisions are traceable and rules can be improved.	3	Medium	QA / Dev
Sprint 4	Monitoring	US-07	As a team lead, I want classification results and exceptions tracked to monitor accuracy and reroutes.	3	Medium	Analyst / QA
Sprint 4	Test & Release	US-08	As a project team, I want representative cases tested and rollout staged to reduce release risk.	5	High	All roles

Planning assumption: 10 working days per sprint; 20 planned story points per sprint. Proposed dates and estimates should be confirmed by the team.

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint 1	20	10 working days	5 Oct 2026	16 Oct 2026	Pending	Pending
Sprint 2	20	10 working days	19 Oct 2026	30 Oct 2026	Pending	Pending
Sprint 3	20	10 working days	2 Nov 2026	13 Nov 2026	Pending	Pending
Sprint 4	20	10 working days	16 Nov 2026	27 Nov 2026	Pending	Pending

Velocity:


Planning estimate: 20 story points over a 10-working-day sprint. Planned average velocity is 2 story points per working day. Actual velocity should be recalculated from accepted completed work; completed points and actual release dates remain pending.

$$\text{Planned velocity} = 20 \text{ story points} \div 10 \text{ working days} = 2 \text{ points/day}$$

Assumption: this is a planning baseline, not measured team performance. Adjust sprint scope after capacity and dependencies are confirmed.

Burndown Chart:

A burndown chart shows remaining work over time. For this plan, the curve below is an illustrative ideal line for one 20-point, 10-working-day sprint, not actual progress. During delivery, update remaining points from the sprint board each working day; compare actual progress with the ideal line and re-plan when scope or capacity changes.

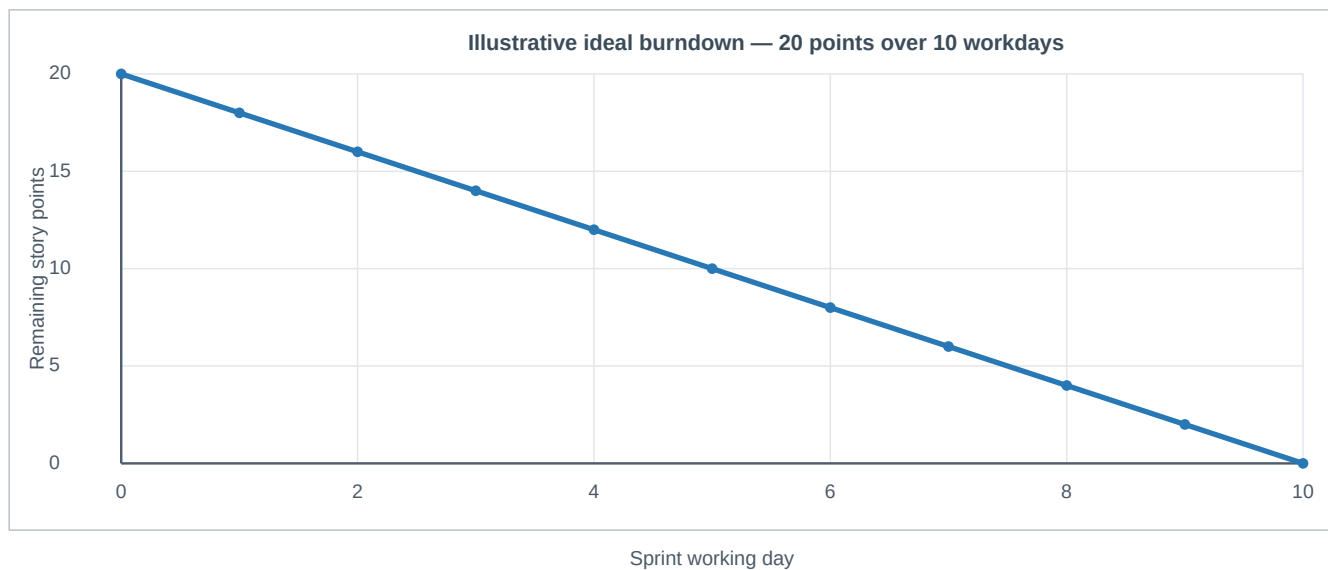

Burndown chart guidance:

<https://www.visual-paradigm.com/scrum/scrum-burndown-chart/>

<https://www.atlassian.com/agile/tutorials/burndown-charts>

Reference:

<https://www.atlassian.com/agile/project-management>

<https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software>

<https://www.atlassian.com/agile/tutorials/epics>

<https://www.atlassian.com/agile/tutorials/sprints>

<https://www.atlassian.com/agile/project-management/estimation>

<https://www.atlassian.com/agile/tutorials/burndown-charts>
